



June 1, 2015

**MEMORANDUM**

1920-15-1  
TO Mayor  
6/15/15

**TO:** James R. McCain, Jr.  
Corporation Secretary/Assistant General Counsel

**THROUGH:** C. Ronald Belton, Assistant to the Mayor/Chief Financial Officer

**FROM:** Thomas G. McKnight *TGM:KT*  
Capital Improvement Construction Manager

**SUBJECT:** Water St. Parking Garage Phase I Improvements: Canopy  
Contractor: Pars Construction Services, LLC  
Contract No: 9424-22

Forwarded herewith for execution is Change Order No. 2 for subject project.

Original Contract Amount .....	\$329,271.00
Previous Change Order No. 1.....	\$17,100.78
Change Order No. 2 .....	\$4,823.51
Total Revised Contract Amount.....	\$351,195.29
Account Number .....	See attached

This office recommends the Change Order be approved by your office, the Office of General Counsel, and Mayor Brown, in accordance with Executive Order No. 13-05.

- Attachments: 1. Change Order  
2. Back-up Information  
3. Legal Request Memorandum

TGM:lw



CHANGE ORDER TRACKING SHEET


Description of Project	Water St Parking Garage Canopy	
Change Order Number	2	PLEASE KEEP THIS FORM WITH THE ATTACHED CHANGE ORDER
Contract Number	9424-22	

	Action	Date Received	Date Signed	Date Forwarded	Signature	Days
1	Date Initiated	N/A	N/A			
1A						
2	Contractor Execution					
3	Construction Management	5/20/15				
4	Using Agency					
5	JEA (if applicable)					
6	City Engineer	6/1	6/1			
7	C/O Review	Dum	Dum	6/10/15	<del>DLT</del>	
8	Director of Public Works	6/1	6/1			
9	Admin/Finance Clerk	6/9	6/10	6/10	[Signature]	
10	Buyer	6/10	6/11	6/11	[Signature]	
11	Chief of Procurement					
12	Director Finance					
13	Asst. General Counsel					
14	CAO/Mayor					
15	Asst. General Counsel					
	Total Processing Days:					

Attention Change Order reviewers and signatories:

Please assist in expediting this change order by reviewing, signing, and forwarding immediately to the next step. Thank you in advance for your efforts to reduce contract change order processing times.

James M. Robinson, P.E.  
Director of Public Works



CITY OF JACKSONVILLE  
DEPARTMENT OF PUBLIC WORKS  
ENGINEERING DIVISION  
CONSTRUCTION CHANGE ORDER

Change Order No. Two (2) April 29, 2015

Description of Project Water Street Parking Garage Phase I Improvements: Canopy

Name of Contractor Pars Construction Services, LLC

Contractor's Address 7643 Gate Parkway Suite 104-82, Jacksonville, FL 32256

Contract No. 9424-22

Account No. See attached. Original Contract \$329,271.00 ✓

+ Previous Change Order 1 \$17,100.78 ✓ + Change Order No. 2 \$4,823.51 ✓

\*See attached appendix for additional listings.

TOTAL REVISED CONTRACT \$351,195.29 ✓

Bid Number JCF-0069-14 Construction Completion Date December 20, 2014

Revised Construction Completion Date May 31, 2015

Contract Expiration Date April 19, 2015

Revised Contract Expiration Date September 28, 2015

In compliance with General Conditions of above-referenced contract, CONTRACTOR and OWNER do both hereby agree that the CONTRACTOR shall make the following changes, additions or deletions to the Work specified in the plans and specifications: See attached. Add 162 non-compensable calendar days to construction completion and contract expiration dates.

Justification: See attached.

By execution of this document, the Contractor acknowledges that all issues related to Contract Time and Compensation are resolved.

The Issuing Authority has looked over cost and pricing data for this change order and has determined that this change order is necessary and all costs are reasonable.

Accepted for Contractor Pars Construction Services, LLC

Signed [Signature] Attest April D. Campbell

Title President Title Project Manager

Date 5-14-15 Date 5-14-15

Signed Construction Management By [Signature] 5-27-15

Issuing Authority Thomas G. McKnight Date  
Capital Improvement Construction Manager

Signed Public Buildings By [Signature] 5/28/15

Using Division Div/Department Head Date

[Signature] 6/6/15 [Signature] 6-16-15

Chief Engineering & Construction Mgmt Div Date Assistant Counsel Date

[Signature] 6/1/15 [Signature] 6/18/15

Director of Public Works Date Mayor Date


[Signature] 6/16/15 [Signature] 6-19-15

Chief of Procurement Date Corporation Secretary

[Signature] 4/15/15

Director of Finance Date

Cleveland Ferguson III  
Deputy Chief Administrative Officer  
For: Mayor Alvin Brown  
Under Authority of:  
Executive Order No. 2015-01



9424-22C/02  
[Handwritten initials]

THE UNIVERSITY OF CHICAGO  
DEPARTMENT OF POLITICAL SCIENCE  
OFFICE OF THE DEPARTMENT CHAIR

Dear Mr. [Name]:

I am pleased to hear that you are interested in the Department of Political Science at the University of Chicago. We have a strong and growing program in your field, and we would like to discuss the possibility of your joining our faculty.

The Department of Political Science at the University of Chicago is one of the leading departments in the world. We have a long and distinguished history, and we are currently enjoying a period of rapid growth. Our faculty is made up of some of the best minds in the field, and we have a wide range of research interests. We would like to see if your research interests align with ours.

We are currently looking for someone who is interested in [Field] and who has a strong background in [Field]. We would like to see your curriculum vitae and a letter of recommendation from a colleague in your field. If you are interested, please send these materials to the Department Chair, [Name], at the University of Chicago, [Address].

We would like to schedule a meeting with you to discuss the possibility of your joining our faculty. Please let us know if you are available for a meeting on [Date]. We would like to meet with you at the University of Chicago, [Address].

We are very interested in your work and would like to see if you would be a good fit for our department. We would like to see your curriculum vitae and a letter of recommendation from a colleague in your field. If you are interested, please send these materials to the Department Chair, [Name], at the University of Chicago, [Address].

We would like to schedule a meeting with you to discuss the possibility of your joining our faculty. Please let us know if you are available for a meeting on [Date]. We would like to meet with you at the University of Chicago, [Address].

We are very interested in your work and would like to see if you would be a good fit for our department. We would like to see your curriculum vitae and a letter of recommendation from a colleague in your field. If you are interested, please send these materials to the Department Chair, [Name], at the University of Chicago, [Address].



Very truly yours,  
[Name]  
Department Chair

SUBJECT: PHASE 1 IMPROVEMENTS OF THE WATER STREET PARKING GARAGE

BID# JCF-0069-14

OPEN DATE: 2014-04-30

**GENERAL GOVERNMENT AWARDS COMMITTEE**

KIND AND BASIS OF CONTRACT:

JSEB SET-ASIDE

AGENCY: **PUBLIC WORKS**

BASIS OF AWARD: **LOWEST RESPONSIVE, RESPONSIBLE BIDDER- LUMP SUM BASE BID**

NUMBER OF BIDS INVITED 4 NUMBER RECEIVED 4 OTHER 0

**SUMMARY OF BIDS AND RECOMMENDED ACTIONS:**

Subject bid was awarded on 06/12/14 to Pars Construction Services, LLC.(contract #9424-22), in the amount of \$329,271.00; Amended on 06/27/14 to waive bonds; Change Order # 1 was administratively approved in the amount of \$17,100.78.

Recommend approval of Change Order #2 to Pars Construction Services, LLC., in the amount of \$4,823.51, for a revised total estimated expenditure not-to-exceed \$351,195.29.

Funding for this award to be encumbered by account: PWCP329PB519-069505-PW0320-02 to be executed by contract change order #2 through Office of General Counsel.

Attachments: Recommendation Memo, Change Order, Previous Award(s)

BUYER: Marilyn Laidler  
MARILYN LAIDLER

RESPECTFULLY SUBMITTED: Gregory Pease  
GREGORY PEASE, CHIEF  
PROCUREMENT DIVISION

CONCURRENCE BY: William J. Joyce, P.E., Chief, Engineering and Construction Management Division

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**

ACTION OF GGAC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 3 MEMBERS DISAPPROVING \_\_\_\_\_ DATE: 05/21/15

OTHER: \_\_\_\_\_

ACTION OF AWARDING AUTHORITY DATE: 5/21/15

APPROVED EA DISAPPROVED \_\_\_\_\_

OTHER \_\_\_\_\_

SIGNATURE OF AUTHENTICATION CPPL

Cleveland Ferguson III  
Deputy Chief Administrative Officer  
For: Mayor Alvin Brown  
Under Authority of:  
Executive Order No. 2015-01





ATTACHMENT "A"  
ACCOUNT NUMBERS  
WATER ST PARKING GARAGE PHASE I CANOPY

ACCOUNT NO.	PWCP363PB519-06505-PW0320-02	PWCP329PB519-069505-PW0320-02	Contract Totals
CT NO.	CTPW14000045-01	CTPW14000045-02	
original contract	\$277,544.27	\$51,726.73	\$329,271.00
change order #1	\$0.00	\$17,100.78	\$17,100.78
change order #2	\$0.00	\$4,823.51	\$4,823.51
Account Totals	\$277,544.27	\$73,651.02	\$351,195.29



NBR	MASTER ITEM DESCRIPTION	QUANTITY	UOM	UNIT COST	NET ADDITION	NET DELETION	TOTALS
-----	-------------------------	----------	-----	-----------	--------------	--------------	--------

**ADDITIONAL SCOPE**

1	REMOVE & REPLACE SECTION OF SIDEWALK AROUND 2 UTILITY BOXES	1	LS	\$2,882.78	\$2,882.78		
---	---	---	----	------------	------------	--	--

JUSTIFICATION: Sidewalk adjacent to project is around 2 utility boxes and has many cracks. The client requested that the additional sidewalk be added so that there is no broken sidewalk next to the new work.

4	ADDITIONAL #5 REBAR FOR COLUMNS	1	LS	\$ 949.96	\$949.96		
---	---------------------------------	---	----	-----------	----------	--	--

JUSTIFICATION: Additional rebar added to columns to increase structural integrity of the canopy to strengthen wind resistance.

**TOTAL ADDITIONAL SCOPE** **\$3,832.74**

**UNFORESEEN CONDITIONS**

2	REPLACE 2" " PVC DRAINAGE PIPE FOR STORM DRAINAGE PUMP FOUND ENCASED IN 12" CONCRETE SLAB REMOVED WITH C/O 2.	1	LS	\$638.03	\$638.03		
---	---	---	----	----------	----------	--	--

JUSTIFICATION: During demolition, the contractor encountered a 12" thick reinforced concrete slab underneath the 4" sidewalk, that had to be removed in order to proceed with the project. Encased in this slab was a 2" PVC drain line pipe attached to a pump located in the stormwater vault, required for if/when the water level reaches a certain height in order to drain the vault. There was no way to remove the concrete without damaging the PVC pipe.


3	CHANGE MATERIALS USED AROUND THE EDGE OF EXISTING DRAINAGE VAULT IN SIDEWALK.	1	LS	\$352.74	\$352.74		
---	---	---	----	----------	----------	--	--

JUSTIFICATION: The original plan was to pour new concrete sidewalk around the edge of the drainage vault. However, once the existing sidewalk was removed it was discovered that there was insufficient depth (1") from the top of the vault to pour concrete back over it that would be thick enough to not break, so a different material was used instead (Tammspatch II). The alternative would have been to cut down the top of the vault to increase the depth.

**TOTAL UNFORESEEN CONDITIONS:** **\$990.77**

TOTAL CHANGE ORDER # 2	\$ 4,823.51	\$ -
<b>TOTAL NET CHANGE ORDER</b>	<b>\$ 4,823.51</b>	





PARS CONSTRUCTION SERVICES

September 2, 2014

Mr. Bill Bishop  
City of Jacksonville  
Public Works – Construction Management Section  
214 N. Hogan Street, 10th Floor  
Jacksonville, FL 32202

**Re: PCO #1 – Removal of Extra Sidewalk Along Bay Street with 8" Brick Band  
JCF-0069-14 ~ Water Street Parking Garage Phase I Improvements & Canopy**

Dear Mr. Bishop -

As a follow-up to our email dated August 26, 2014, Pars Construction Services submits the attached cost proposal for removal and replacement of the existing concrete sidewalk at the west side of the project where the two (2) water meters are located for aesthetic purposes. Pars Construction Services (PCS) is submitting this change order request for additional work associated with this added scope and respectfully requests approval of this change order request in the amount of **TWO THOUSAND EIGHT HUNDRED EIGHTY-TWO DOLLARS AND SEVENTY-EIGHT CENTS (\$2,882.78).**

If you should have any questions, please do not hesitate to call our office.

Professionally,

Pars Construction Services, LLC.

Ali Hakimi  
President

cc: PCO 1 File

**Subject:** Water Street Parking Garage - Unforeseen Condition  
**From:** Ali Hakimi (ahakimi@pars-construction.com)  
**To:** WHBishop@coj.net;  
**Cc:** MariaCW@coj.net; acampbell@pars-construction.com;  
**Date:** Tuesday, August 26, 2014 9:28 PM

Bill -

Please accept this email as documentation and follow-up to recapture the onsite meeting on 8-21-14 relating to the unforeseen condition encountered at the subject project. While removing the 4" sidewalk, it was discovered that there was an existing 12" reinforced concrete slab underneath the sidewalk. It was determined by the EOR that the 12" reinforced concrete slab had to be removed. Therefore, please be advised that there will be additional costs and schedule impacts related to the removal of this unforeseen condition.

Also, Pars was requested by COJ to provide a cost proposal for removal and replacement of the existing concrete sidewalk at the west side of the project where the two (2) water meters are located for aesthetic purposes.

*Professionally,*

Ali Hakimi  
**Pars Construction**  
7643 Gale Parkway, Suite 104-82  
Jacksonville, FL 32256  
Phone: (904)-642-6144  
Fax: (904)-527-1014  
Direct Line: (904)-505-5621  
ahakimi@pars-construction.com



PHRS CONSTRUCTION SERVICES

PCO #1 - Removal of Extra Sidewalk Along Bay Street with 8" Brick Band  
 Water Street Parking Garage Phase I Improvements & Canopy

<u>Labor</u>						
Foreman	10	HRS	@	\$32.00	PER HR	\$320.00
Operator	10	HRS	@	\$22.00	PER HR	\$220.00
Laborer	10	HRS	@	\$17.00	PER HR	\$170.00
					Sub Total	\$710.00
					47.46% Burden	\$336.97
					Subtotal Costs	\$1,046.97
					Mark Up 15%	\$157.04
					Total Labor	\$1,204.01
Foreman Truck w/tools	10	HRS	@	\$21.98	PER HR	\$219.80
Jack Hammer & Compressor	1	DAY	@	\$250.00	DAY	\$ 250.00
Concrete Saw and Blade	1	LS	@	\$150.00	LUMP SUM	\$ 150.00
Concrete Removal	1	LS	@	\$250.00	LUMP SUM	\$ 250.00
Concrete Subbase	1	LS	@	\$350.00	LUMP SUM	\$ 350.00
Brick Band	1	LS	@	\$240.00	LUMP SUM	\$ 240.00
					Subtotal Equipment	\$1,459.80
					Mark Up 15%	\$218.97
					Total Equipment	\$1,678.77
<b>GRAND TOTAL</b>						<b>\$2,882.78</b>



PARS CONSTRUCTION SERVICES

February 9, 2015

Mr. Bill Bishop  
City of Jacksonville  
Public Works – Construction Management Section  
214 N. Hogan Street, 10th Floor  
Jacksonville, FL 32202

**Re: PCO #6 – Additional Support for Canopy Modifications  
JCF-0069-14 ~ Water Street Parking Garage Phase I Improvements & Canopy**

Dear Mr. Bishop -

In response to the attached Atlantic Engineer Services letter dated January 16, 2015, we herein provide our cost proposal for additional canopy support modifications. The following modifications of the columns are required:

- 1.) At the two columns where the footing already has been poured, add 6-#5 dowels drilled and epoxied anchored with Hilti HY 200 with 12" minimum embedment.
- 2.) At the two columns where the footing has not been poured, add 4-#5 bent dowels.
- 3.) Revise the vertical reinforcing for all four columns to 10-#5.

Pars Construction Services (PCS) is submitting this change order request for additional work associated with this added scope and respectfully requests approval of this change order request in the amount of **NINE HUNDRED FORTY-NINE DOLLARS AND NINETY-SIX CENTS (\$949.96).**

If you should have any questions, please do not hesitate to call our office.

Professionally,

Pars Construction Services, LLC.

A handwritten signature in black ink, appearing to read 'Ali Hakimi', is written over a horizontal line.

Ali Hakimi  
President

cc: PCO 6 File





**ATLANTIC  
ENGINEERING**

6511 Arlington Express  
Building B, Suite 201  
Jacksonville, FL 32211  
PH: 904.743.4932  
FX: 904.795.9229  
jackson@aes.com  
www.aes.com

January 16, 2015

Mr. Stephen F. Lazar, AIA, LEED AP  
VRL Architects, Inc.  
1449 Palm Avenue  
Jacksonville, FL 32207-8467

Re: Water Street Parking Garage Canopies

Project: #310-279.04

Dear Steve:

A typo was discovered on the structural drawings while reviewing shop drawing for the canopies. The structural drawings currently specify 6-#5 vertical for the concrete columns supporting the canopy. These columns require 10 #5 vertical in lieu of the 6-#5 specified. The footing supporting the columns at the north end have already been poured and at the south end the contractor is in the process of installing the reinforcing mat for the footing. Also, while on site today at one of the north end columns, two dowels were short and do not have the required lap length.

The following modifications of the columns are required:

- a. At the two columns where the footing already has been poured, add 6-#5 dowels drilled and epoxied anchored with Hilti HY 200 with 12" minimum embedment.
- b. At the two columns where the footing has not been poured, add 4-#5 bent dowels.
- c. Revise the vertical reinforcing for all four columns to 10-#5.

Please contact our office if there are any questions regarding this correspondence, or if you need any additional information or assistance.

Very truly yours,  
ATLANTIC ENGINEERING SERVICES OF JACKSONVILLE  
FLORIDA CERTIFICATE OF AUTHORIZATION #791

Jude T. Kostage, P.E.  
Senior Project Engineer

JTK



PIRS CONSTRUCTION SERVICES

PCO #6 - Additional Support for Canopy Modifications  
Water Street Parking Garage Phase I Improvements & Canopy

<u>Labor</u>							
Foreman	4	HRS	@	\$32.00	PER HR	\$	128.00
Laborer	8	HRS	@	\$17.00	PER HR	\$	136.00
					Sub Total	\$	264.00
					47.46% Burden	\$	125.29
					Subtotal Costs	\$	389.29
					Mark Up 15%	\$	58.39
					Total Labor	\$	447.69
<u>Equipment</u>							
Foreman Truck w/tools	4	HRS	@	\$21.98	PER HR	\$	87.92
Drill Hammer	1	DAY	@	\$70.62	PER DAY	\$	70.62
1" Rock Drill Bit	1	DAY	@	\$8.56	PER DAY	\$	8.56
Generator	1	DAY	@	\$63.13	PER DAY	\$	63.13
					Subtotal Equipment	\$	230.23
					Mark Up 15%	\$	34.53
					Total Equipment	\$	264.76
<u>Material</u>							
Rebar	20	EA	@	\$7.76	EACH	\$	155.20
Epoxy	1	EA	@	\$51.33	EACH	\$	51.33
					Subtotal Material	\$	206.53
					Mark Up 15%	\$	30.98
					Total Material	\$	237.51
					<b>GRAND TOTAL</b>	<b>\$</b>	<b>949.96</b>



Account | My Account | Sign In | Sign Up

Home | Equipment | Locations | Customer Service | About | My Account

Equipment | Locations | Customer Service | About | My Account

Equipment > General Construction Tools > Electric Tools > Rotary and Demolition Hammers

## 25lb Class Demolition Hammer

### Your Cart

No items in your cart

To see availability please enter ZIP code. Address will auto populate when you select a location. **32256**



Know what equipment you need? [Take our quiz](#)



### Rental Rates

Equipment pricing may vary based on availability and market conditions

\$46 4 Hour   **\$66 Daily**   \$210 Weekly   \$525 4 Week

TAX  
\$70.62

### Rental Protection Plan



Learn more about our Rental Protection Plan

[Review Our Plans](#)

View our Special Offers

Safety

### Make / Models

Hilti TE-905  
Bosch 11316EVS

### Specifications


Cat Class	120 0110
Amp Rating	13.9 - 14.0
Impact Range	2200 bpm - 909-1890 bpm
Length	23" - 27"
Max Impact Energy/Blow	12.5ft lbs - 15.4ft lbs
Tool Type	SDS-max TE S
Weight	23lbs - 25lbs

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location

A member of our team will contact you within 2 business hours with confirmation of your reservation

Home | Equipment | Locations | Customer Service | About | Site Map | | Find us on Facebook





Account: [Sign In](#) | [Sign Up](#)

Customer Service: [1-800-368-7263](#)

[Equipment](#) | [Locations](#) | [Customer Service](#) | [About](#) | [My Account](#)

### Your Cart

No items in your cart

Equipment > Air Compressors and Air Tools > Air Tools - Demolition > Rock Drills  
1" Integral Carbide Rock Drill Bit

To rent equipment faster, please enter City, State, Address, or ZIP code above. Search by using the equipment?

32256

Search for part # 1500210

#### Rental Rates

Equipment pricing may vary based on availability and market conditions

\$8  
4 Hour

\$8  
Daily

\$19  
Weekly

\$56  
4 Week

Tax  
\$8.56

#### Rental Protection Plan



Learn more about our Rental Protection Plan

#### Review Our Plans

#### General Specifications

##### Make / Models

Varies

##### Specifications

Cat-Class


150-0210

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location.

A member of our team will contact you within 2 business hours with confirmation of your reservation

Home | [Equipment](#) | [Locations](#) | [Customer Service](#) | [About](#) | [Site Map](#) | [Twitter](#) | [LinkedIn](#) | [Facebook](#) | [Find us on Facebook](#)





Sign In Sign Up

1-800-451-7273

3600 Watt Generator

Home

Equipment

Locations

Customer Service

About

My Account

Equipment > Generators and Accessories > Generators > Portable Generators - Gas > 5kW - 10kW

### 3600 Watt Generator


### Your Cart

No items in your cart

To see equipment rates, please enter a zip code. Zip code: 32256



Home > Equipment > 3600 Watt Generator



#### Rental Rates

Equipment pricing may vary based on availability and market conditions

\$44  
4 Hour

\$59  
Daily

\$210  
Weekly

\$555  
4 Week

TA x \$4.13  
\$63.13



#### Rental Protection Plan



Learn more about our Rental Protection Plan

Review Our Plans

View Item Specifications

#### Make / Models

Varies

#### Specifications

Cal-Class

008-0002

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location.

A member of our team will contact you within 2 business hours with confirmation of your reservation.

Home | Equipment | Locations | Customer Service | About | Site Map



Find us on Facebook



Contract Holder




More doing

Store Jacksonville #6346  
Use My Current Location or

Tool & Truck Rental Installation Services and Repair Gift Cards Help

Model # 182478 Internet # 202090264 Store SKU # 393401  
**5/8 in. x 10 ft. Rebar**

Write the First Review Ask a Question

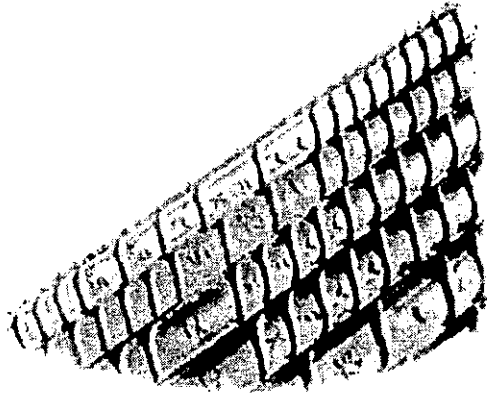

\$7.25 / each +  
\$ 0.51 TAX  
\$ 7.76

ACCESSORIES (4)

YOUR CURRENT PRODUCT


1 of 2



\$7.25 / each

5/8 in. x 10 ft. Rebar

Item Selected



\$2.97 / each

The Home Depot 5-gal.  
Homer Bucket

(96)

Select This Item



\$7.50 / each

Marshalltown Masonry Brush

(2)

Select This Item



\$7.25 / each

Marshalltown 6 in. x 4 in.  
Steel Edger

(4)

Select This Item

1 Item(s) Selected

ADD ITEMS TO CART

PRODUCT OVERVIEW Model # 182478 Internet # 202090264 Store SKU # 393401

The 5/8 in. x 10 ft. Rebar is made from Grade 40 steel for strength and durability. The rebar can be used in concrete reinforcement or expansion applications.

- Made from Grade 40 steel
- Can be used in concrete reinforcement or expansion applications
- Designed with ridges for ideal mechanical anchoring
- Features a minimum yield strength of 80,000 psi
- Note: Product may vary by store




More info  
More doing

Search for Jacksonville #6346  
Use My Current Location or My Location

Tool & Truck Rental Installation Services and Repair Gift Cards Help

Hilti Model # 3508711 Internet # 205476518  
**HIT HY 200-R Injectable Mortar**

Write the First Review

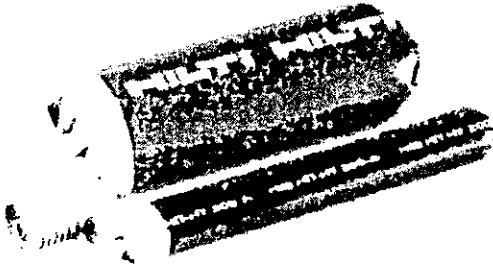

\$47.98 /each +  
\$ 3.35 TAX  
-----  
\$ 51.33

**PRODUCT OVERVIEW** Model # 3508711 Internet # 205476518

Hilti HIT-HY 200-R is the latest generation of the industry leading line of injectable adhesive for concrete. Product is ICC-ES approved for use in both cracked and uncracked concrete applications. Contractors experience less down time, as the flexibility of the product allows for installation in both wet and dry conditions, as well as a wide temperature range. The HY 200-R can be used for a variety of applications which include anchoring steel columns, beams, racking, guard rails and sound barriers. It can also be used for seismic strengthening, retrofitting and bracing of reinforced concrete buildings. Hilti's HIT HY 200-R represents Hilti's latest innovation based on decades of industry-leading knowledge and experience.

- Use to anchor rods, rebar and threaded inserts into concrete quickly and effectively
- Working time optimized for rebar and deep anchoring applications
- Highest level of approval in concrete for cracked and uncracked applications
- Contractors can select the ideal working time based on application and temperature conditions
- Use with the Hilti HDM 500 manual adhesive dispenser (sold separately)
- Includes (1) 11.1 oz. foil pack with (1) mixer and (1) 3/8 in. mixer extension
- Note: product may vary by store


**SPECIFICATIONS**

**DIMENSIONS**

Assembled Depth (in.)	12 in	Assembled Width (in.)	3.5 in
Assembled Height (in.)	2.5 in	Fastener length (in.)	12

**DETAILS**

Cure time (hours)	20	Maximum stable temperature (Degrees)	104
Fastener Type	Chemical Anchor	Minimum stable temperature (Degrees)	14
Fastener/Connector Material	Steel	Package Quantity	1
Finish Family	Gray	Primary Use	Fastening into concrete
Hazardous Code	No Air	Product Weight (lb.)	1 lb
Indoor/Outdoor	Indoor/Outdoor	Returnable	90-Day
Maximum Weight Capacity (lb.)	0	Volume (oz.)	11.1



PARS CONSTRUCTION SERVICES

January 26, 2015

Mr. Bill Bishop  
City of Jacksonville  
Public Works – Construction Management Section  
214 N. Hogan Street, 10th Floor  
Jacksonville, FL 32202

Re: **PCO #4 – RFI #5 Replacement of 2" PVC Drain  
JCF-0069-14 – Water Street Parking Garage Phase I Improvements & Canopy**

Dear Mr. Bishop -

As a follow-up to RFI #5, there is an existing PVC pipe which runs into the pump at the existing storm structure. This pipe was encased to 16" into the existing concrete sidewalk. During the removal of the existing sidewalk, said pipe was removed. The response to the subject RFI is to replace the demoed PVC pipe and repairing the portion of the existing curb which is penetrated by the discharge PVC pipe and replacement of the adjacent broken concrete curb.

Pars Construction Services (PCS) is submitting this change order request for additional work associated with this added scope and respectfully requests approval of this change order request in the amount of **SIX HUNDRED THIRTY-EIGHT DOLLARS AND THREE CENTS (\$638.03)**.

If you should have any questions, please do not hesitate to call our office.

Professionally,

Pars Construction Services, LLC.

A handwritten signature in black ink, appearing to read 'Ali Hakimi', is written over a horizontal line.

Ali Hakimi  
President

cc: PCO 4 File

7643 Oaic Parkway, Suite 104-82  
Jacksonville, FL 32256  
904-642-6144 ~ 904-527-1014 fax  
[www.pars-construction.com](http://www.pars-construction.com)  
CGC 1514726



**REQUEST FOR INFORMATION (RFI)**

PROJECT: Water Street Parking Garage

DATE: 12-29-14

RFI #or NOI #: Five (5)

CONTRACTOR: Pars Construction Services, LLC

SPEC REF: \_\_\_\_\_

CONTRACT/P.O. #: 9424-22

DWG REF: \_\_\_\_\_

RFI OR NOI DESCRIPTION: \_\_\_\_\_

There is an existing discharge PVC pipe which runs into the pump at the existing storm structure. This pipe was increased to 16" into the existing concrete sidewalk. During the removal of the existing sidewalk, said pipe was also removed. During today's site meeting with COJ and V.R.L. this was brought to the attention of all parties. Please advise.

SUBMITTED BY: Ali Hakimi

Contractor's Representative

REQUEST REPLY BY: \_\_\_\_\_

REPLY: THE PVC PIPE APPEARS TO BE 2"  $\phi$ . THIS PIPE WAS NOT LOCATED BY JEA AND IS A DISCOVERED CONDITION WHICH MUST BE REPLAZED DURING THIS CONSTRUCTION. ASSOCIATED WITH THIS REPLACEMENT, WE RECOMMEND REPAIRING THE PORTION OF EXISTING CURB WHICH IS PENETRATED BY THE DISCHARGE PVC PIPE. A PORTION OF BROKEN, ADJACENT CONCRETE CURB SHOULD ALSO BE REPLAZED.

REPLY BY: \_\_\_\_\_

STEPHEN F. LAZAR, A.I.A.  
Owner's Representative

DATE: 30 DEC 2014

REPLAZED.

This reply does not necessarily constitute an increase in contract value or time. Any Change in contract value or time will require supplemental information submitted by the contractor for review and approval.











PCS  
PARRS CONSTRUCTION SERVICES

PCO #4 - RFI #5 Replace 2" PVC Pipe  
Water Street Parking Garage Phase I Improvements & Canopy

<b>Replacing 2" PVC Pipe</b>						
<u>Labor</u>						
Plumber	4	HRS	@	\$16.00	PER HR	\$ 64.00
					Sub Total	\$ 64.00
					47.46% Burden	\$ 30.37
					Subtotal Costs	\$ 94.37
					Mark Up 15%	\$ 14.16
					Total Labor	\$ 108.53
<b>Material - Replacing 2" PVC Pipe</b>						
PVC Pipe	10	LF	@	\$2.49	PER HR	\$ 24.90
2" PVC Fitting	4	EA	@	\$0.90	EACH	\$ 3.60
Plumbing Cement	1	EA	@	\$4.87	EACH	\$ 4.87
					Subtotal Material	\$ 33.37
					Sales Tax	\$ 2.34
					Subtotal Material	\$ 35.71
					Mark Up 15%	\$ 5.36
					Total Material	\$ 41.06
<b>Material - Concrete Materials for Curb Repair</b>						
5 Bags of Ready Mix	5	EA	@	\$3.95	EA	\$ 19.75
					Subtotal Material	\$ 19.75
					Sales Tax	\$ 1.38
					Subtotal Material	\$ 21.13
					Mark Up 15%	\$ 3.17
					Total Material	\$ 24.30
<b>Demo Existing Concrete Curb &amp; Pour Back</b>						
<u>Labor</u>						
Laborer	8	HRS	@	\$17.00	PER HR	\$ 136.00
Finisher	4	HRS	@	\$21.00	PER HR	\$ 84.00
					Sub Total	\$ 220.00
					47.46% Burden	\$ 104.41
					Subtotal Costs	\$ 324.41
					Mark Up 15%	\$ 48.66
					Total Labor	\$ 373.07
<b>Equipment</b>						
12" Gas Cutoff Saw (minimum 4 hours)	1	EA	@	\$37.00	EA	\$ 37.00
Demolition Hammer (minimum 4 hours)	1	EA	@	\$37.00	EA	\$ 37.00
					Subtotal Equipment	\$ 74.00
					Sales Tax	\$ 5.18
					Subtotal Equipment	\$ 79.18
					Mark Up 15%	\$ 11.88
					Total Equipment	\$ 91.06
					<b>GRAND TOTAL</b>	<b>\$ 638.03</b>

Your Store: **Southside** (Change)

Open Until: 8:00 pm



Shop By Department ▾

VPC | Model #: 2202

# 2 in. x 2 ft. PVC-PW Sch. 40 DWV Pipe

Not Yet Rated

Write a Review +

~~\$4.98~~ 5 = \$24.90

**\$4.98** / each



Item must be picked up in store


**Pick Up In Store FREE**

Available for Pick Up: **TODAY**

60 In Stock at

**Southside Store**

Pick Up at Another Store



- 1 +

ADD TO CART

SAVE MY LI



**IN STOCK AT YOUR SELECTED STORE**

**Southside #226**

**60** In Stock

Jacksonville, FL 32256

In-Store Map +

Change Pick Up Store +

PRODUCT OVERVIEW ▾

SPECIFICATIONS ▾

RECOMMENDED PRODUCTS ▾

## PRODUCT OVERVIEW

Model: # 2202 | Internet/Catalog: # 202300507 | Store SKU: # 276902 | Store SO SKU: #

111024

The VPC 2 in. x 2 ft. PVC-PW Sch. 40 DWV Pipe can be used in systems with temperatures up to 140 degrees Fahrenheit. It is

**Info & Guides**



Your Store: **Southside** (Change)

Open Until: **8:00 pm**



Shop By  
**Department** ▾

Mueller Streamline | Model #: 05886H

# 2 in. PVC DWV 45-Degree Hub x Hub Elbow

Not Yet Rated

Write a Review +

**\$0.99** / each



Item must be picked up in store

**Pick Up In Store FREE**

Available for Pick Up: **TODAY**

**19** In Stock at

**Southside Store**

Pick Up at Another Store

- 1 +

**ADD TO CART**

**SAVE MY LIST**



**IN STOCK AT YOUR SELECTED STORE**



**Southside #226**

**19** In Stock

Jacksonville, FL 32256 Aisle 35, Bay 010

**Change Pick Up Store + In-Store Map +**

**PRODUCT OVERVIEW** ▾

**SPECIFICATIONS** ▾

**RECOMMENDED PRODUCTS** ▾

## PRODUCT OVERVIEW

Model: # 05886H | Internet/Catalog: # 204840560 | Store SKU: # 189340

The Mueller Streamline 2 in. PVC DWV 45-Degree Hub x Hub Elbow is utilized for a non-pressurized DWV sanitary system. It changes the direction of PVC piping by 45 degrees. This product is

**Info & Guides**

**Warranty**



PRODUCT OVERVIEW ▾

SPECIFICATIONS ▾

RECOMMENDED PRODUCTS ▾

CUSTOMER REVIEWS

Your Store: **Southside** (Change) Open Until: 8:00 pm



Shop By Department ▾




# 4 oz. ABS to PVC Transition Cement

Not Yet Rated

Write a Review +

**\$4.87** / each



Ship to Home FREE with \$45 Order

Est. Arrival Date: FEB 3 - FEB 5

Pick Up In Store FREE

Available for Pick Up: TODAY

- 1 +

ADD TO CART

SAVE MY LIST

This item cannot be shipped to the following state(s): AK, CA, GU, HI, PR, VI



**IN STOCK AT YOUR SELECTED STORE**

Southside #226

**8** In Stock

Jacksonville, FL 32256 Aisle 35, Bay 002

Change Pick Up Store + In-Store Map +

PRODUCT OVERVIEW ▾

SPECIFICATIONS ▾

RECOMMENDED PRODUCTS ▾

## PRODUCT OVERVIEW

Model: # 309003 | Internet/Catalog: # 100344275 | Store SKU: # 300195 | Store SO

SKU: # 125490



More buying  
More doing

Your Store **Jacksonville #6346**  
Use My Current Location or find store

Tool & Truck Rental   Installation Services and Repair   Gift Cards   Help

**SAKRETE** Model # 65200390   Internet # 100350291   Store SKU # 533829  
**80 lb. Gray Concrete Mix**

★ ★ ★ (15)   Customer Images (2)   Write a Review   Questions & Answers (19)

**\$3.95** /each (limit 56 per order)



**ACCESSORIES (8)**

YOUR CURRENT PRODUCT

1 of 3




**\$3.95** /each

SAKRETE 80 lb. Gray  
Concrete Mix

(15)

Item Selected



**\$59.98** /each

Husky 10 ft. x 100 ft. Black 6  
mil Plastic...

(7)

Select This Item



**\$59.98** /each

Husky 10 ft. x 100 ft. Clear 6  
mil...

Select This Item



**\$98.00** /each

Husky 20 ft. x 100 ft. Black 6  
mil...

(9)

Select This Item


1 Item(s) Selected

**ADD ITEMS TO CART**

**PRODUCT OVERVIEW** Model # 65200390   Internet # 100350291   Store SKU # 533829

A great concrete for all-purpose work, SAKRETE 80 lb. Gray Concrete Mix is suitable for use in setting footings and pouring slabs. This concrete can be applied for anchoring posts and poles as well. Meets ASTM C 387 strength requirements.

- Premium concrete for all purpose applications
- Use for walks, footings, slabs and steps, anchoring posts and poles
- For applications requiring at least 2 in. in thickness
- Approximate 45-minute working time
- 4,000 psi
- Note: Product may vary by store



Welcome to Sunbelt Rentals

[Sign In](#)

[Sign Up](#)

[Send us your feedback](#)

[1-800 No Sweat Rentals](#)

[Checkout](#)

[Equipment](#)

[Locations](#)

[Customer Service](#)

[About](#)

[My Account](#)

Equipment > Concrete and Masonry >  
Concrete / Masonry - Cutting & Drilling Equipment >  
Cutoff Saws Hand Held / Gas / Air / Electric / Hydraulic

## 12" Gas Cutoff Saw

### Your Cart

No items in your cart

To see equipment rates, please enter City, State, Address or ZIP code where you will be using the equipment



Nearest Branch: #007 Jacksonville, FL 32202



### Rental Rates

Equipment pricing may vary based on availability and market conditions

<b>\$37</b> 4 Hour	<b>\$58</b> Daily	<b>\$175</b> Weekly	<b>\$425</b> 4 Week
-----------------------	----------------------	------------------------	------------------------

### Rental Protection Plan



Ensure your peace of mind with the additional coverage provided by Sunbelt Rentals Rental Protection Plan

[Review Our Plans](#)

### General Specifications

#### Make / Models

Varies

#### Specifications

Cat-Class: 020-0020

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location.


A member of our team will contact you within 2 business hours with confirmation of your reservation.

[Home](#) | [Equipment](#) | [Locations](#) | [Customer Service](#) | [About](#) | [Site Map](#)

[Find us on Facebook](#)

© 2015 Sunbelt Rentals, Inc. All Rights Reserved | [Privacy Policy](#) | [Terms and Conditions](#) | Sunbelt Rentals Toll-Free 1-800 No Sweat (800-667-9328)


Site intended for U.S. Customers Only



Welcome to Sunbelt Rentals

[Sign In](#)

[Sign Up](#)



Send us your feedback!

1-800 No Sweat  
1-800-667-9328

Checkout  
0 Items

Search for equipment

[Equipment](#)

[Locations](#)

[Customer Service](#)

[About](#)

[My Account](#)

[Equipment](#) > [General Construction Tools](#) > [Electric Tools](#) > [Rotary and Demolition Hammers](#)

# 12lb Class Demolition Hammer

## Your Cart

No items in your cart

To see equipment rates please enter City, State, Address or ZIP code where you will be using the equipment **32256**



Nearest Branch: #007 - Jacksonville, FL - 32207-1930



### Rental Rates

Equipment pricing may vary based on availability and market conditions.

<b>\$37</b> 4 Hour	<b>\$53</b> Daily	<b>\$190</b> Weekly	<b>\$500</b> 4 Week
-----------------------	----------------------	------------------------	------------------------



### Rental Protection Plan

Ensure your peace of mind with the additional coverage provided by Sunbelt Rentals Rental Protection Plan

### General Specifications Safety

#### Make / Models

- Hilti / TE-505
- Bosch / 11318EVS

#### Specifications

Cat-Class:	120-0100
Amp Rating:	11.0, 7.8
Impact Range:	1300-3300 bpm, 1860/2630 bpm
Length:	17" - 18"
Max. Impact Energy/Blow:	3.8ft. lbs - 8.8ft. lbs
Tool Type:	SDS-max
Weight:	12lbs - 13lbs

### Review Our Plans

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location.

A member of our team will contact you within 2 business hours with confirmation of your reservation.

[Home](#) | [Equipment](#) | [Locations](#) | [Customer Service](#) | [About](#) | [Site Map](#)

[Find us on Facebook](#)

© 2015 Sunbelt Rentals, Inc. All Rights Reserved | [Privacy Policy](#) | [Terms and Conditions](#) | Sunbelt Rentals Toll-Free 1-800 No Sweat (800-667-9328)

Site intended for U.S. Customers Only



PARS CONSTRUCTION SERVICES

January 26, 2015

Mr. Bill Bishop  
City of Jacksonville  
Public Works – Construction Management Section  
214 N. Hogan Street, 10th Floor  
Jacksonville, FL 32202

**Re: PCS #5 – Leveling Material for Top of the Electrical Vault  
JCF-0069-14 ~ Water Street Parking Garage Phase I Improvements & Canopy**

Dear Mr. Bishop -

During a site visit after the preconstruction meeting it was brought up by all parties on how to pour the new sidewalk and tie into the existing electrical vault wall. In accordance with the attached email dated September 4, 2014 from Mr. Steve Lazar, Structural Engineer, we were instructed to use Tammspatch II, two component repair mortar to tie into the existing electrical vault.

Pars Construction Services (PCS) is submitting this change order request for additional work associated with this added scope and respectfully requests approval of this change order request in the amount of **THREE HUNDRED FIFTY-TWO DOLLARS AND SEVENTY-FOUR CENTS (\$352.74)**.

If you should have any questions, please do not hesitate to call our office.

Professionally,

Pars Construction Services, LLC.

A handwritten signature in black ink, appearing to read 'Ali Hakimi', written over a horizontal line.

Ali Hakimi  
President

cc: PCO 5 File



**PCO #5 - Leveling Material for Top of the Electrical Vault  
Water Street Parking Garage Phase I Improvements & Canopy**

<u>Labor to form the edge of the vault</u>						
Carpenter	4	HRS	@	\$21.00	PER HR	\$ 84.00
					Sub Total	\$ 84.00
					47.46% Burden	\$ 39.87
					Subtotal Costs	\$ 123.87
					Mark Up 15%	\$ 18.58
					Total Labor	\$ 142.45
<u>Material &amp; Equipment</u>						
Tammspatch II (per kit - bag & jug) plus freight	2	Sets	@	\$42.47	PER SET	\$ 84.94
Form Materials (5 pieces of 1x4 = 50lf)	5	PC	@	\$8.27	PIECES	\$ 41.35
Concrete Anchors	1	BX	@	\$23.61	BOX	\$ 23.61
Rotary Hammer (4 hours minimum)	1	EA	@	\$21.00	EACH	\$ 21.00
						\$ 170.90
					Sales Tax	\$ 11.96
					Subtotal Equipment	\$ 182.86
					Mark Up 15%	\$ 27.43
					Total Equipment	\$ 210.29
<b>GRAND TOTAL</b>						<b>\$ 352.74</b>

## April Campbell

---

**From:** Bishop, William <WHBishop@coj.net>  
**Sent:** Thursday, September 04, 2014 3:40 PM  
**To:** acampbell@pars-construction.com  
**Subject:** FW: RFI #1/Response  
**Attachments:** Tamms Patch II.pdf; 9424-22 RFI# 1.pdf

RFI 1 response

**From:** Steve Lazar [mailto:sflazar@vrlarchitects.com]  
**Sent:** Thursday, September 04, 2014 7:51 AM  
**To:** Bishop, William  
**Subject:** RE: RFI #1/Response

Bill:

Here is the response to RFI #1 and also the leveling material to be applied to the top of the concrete wall of the electrical vault.

Steve Lazar

**From:** Bishop, William [mailto:WHBishop@coj.net]  
**Sent:** Tuesday, September 02, 2014 4:15 PM  
**To:** sflazar@VRLarchitects.com  
**Subject:** FW: RFI #1

Steve,

See this rfi 1 pertaining to the issue we looked at last week

**From:** April Campbell [mailto:acampbell@pars-construction.com]  
**Sent:** Tuesday, September 02, 2014 4:14 PM  
**To:** Bishop, William  
**Subject:** RFI #1

Bill:

Please see the attached RFI #1 per our meeting with engineers and COJ last week.

Professionally,

April D. Campbell  
Project Manager  
904-642-6144 office  
904-401-5553 cell  
904-527-1014 fax  
[acampbell@pars-construction.com](mailto:acampbell@pars-construction.com)  
[www.pars-construction.com](http://www.pars-construction.com)

# TAMMSPATCH II

## TWO-COMPONENT REPAIR MORTAR AND UNDERLAYMENT

### DESCRIPTION

TAMMSPATCH II is a two-component, polymer-modified, cementitious repair mortar and flowable underlayment. When the two components are combined, TAMMSPATCH II becomes a versatile mortar for numerous applications, due to its ability to be mixed at different consistencies. From flowable to firm, TAMMSPATCH II provides an aesthetically pleasing surface in multiple applications.

### PRIMARY APPLICATIONS

- Resurfacing worn concrete walkways
- Trowelable repair mortar
- Decorative overlays
- Horizontal or vertical repairs
- Pointing mortar joints
- Flowable underlayment

### FEATURES/BENEFITS

- Featheredge to 1" (2.5 cm) per lift neat, 2.5" (6.3 cm) if extended
- Highly durable
- Outstanding bond strength
- High strength
- User friendly
- USDA compliant

### TECHNICAL INFORMATION

#### Material Properties at 75°F (24°C)

Initial Set, hrs.....approx. 1.5 to 3  
Final Set, hrs.....approx. 4 to 5

Compressive strength, psi (MPa) ASTM C 109  
3 days.....2,500 (17.2)  
7 days.....3,800 (26.2)  
28 days.....5,000 (34.5)

Tensile strength, psi (MPa) ASTM C 190  
28 days.....650 (4.5)

Tensile Bond Strength CAN A23.2-6B  
28 days.....Greater than concrete

Flexural strength, psi (MPa) ASTM C 348  
7 days.....700 (4.8)  
28 days.....900 (6.2)

Bond strength, psi (MPa) ASTM C 1042  
28 days.....1450 (10.0)

Shrinkage, % ASTM C 157  
28 days.....-0.023%

Freeze thaw durability factor, ASTM C 666  
300 cycles.....99.4%

### PACKAGING/YIELD

TAMMSPATCH II Part A (powder) is packaged in a 45 lb (20.4 kg) bag. Part B (liquid) is packaged in a 1 gal (3.7 L) jug. A mixed unit will yield approximately 0.42 ft<sup>3</sup> (0.011 m<sup>3</sup>).

### SHELF LIFE

1 year in original, unopened packaging

### SPECIFICATIONS/COMPLIANCES

Canadian MTQ

*Phone quote from Coastal Products  
\$42.47/set @ 2 sets = \$84.94  
2 days delivery from TAMPA.*



The Euclid Chemical Company

19218 Redwood Rd. • Cleveland, OH 44110  
Phone: [216] 531-9222 • Toll-free: [800] 321-7628 • Fax: [216] 531-9596  
www.euclidchemical.com

An RPM Company




HORIZONTAL REPAIR

TAMMSPATCH II

Product Literature # 03 01 30 71





Welcome to Sunbelt Rentals

[Sign In](#)

[Sign Up](#)

[Send us your feedback!](#)

[1 800 No Sweat  
Toll-Free 1-800-667-9328](#)

[Checkout  
& Print](#)

[Equipment](#)

[Locations](#)

[Customer Service](#)

[About](#)

[My Account](#)

Your Cart

No items in your cart

[Equipment](#) > [General Construction Tools](#) > [Electric Tools](#) > [Rotary and Demolition Hammers](#)

# 3/16"-1-1/8" Rotary Combination Hammer

To see equipment rates, please enter City, State, Address or ZIP code where you will be using the equipment

32256



Nearest Branch: #007 - Los Angeles, CA 90007

Rental Rates

Equipment pricing may vary based on availability and market conditions.



<b>\$21</b> 4 Hour	<b>\$37</b> Daily	<b>\$98</b> Weekly	<b>\$275</b> 4 Week
-----------------------	----------------------	-----------------------	------------------------

Rental Protection Plan



Extend your rental period with the additional coverage provided by Sunbelt Rentals Rental Protection Plan

Review Our Plans

General Specifications

Safety

Make / Models

- Hilti / TE-6C\*\*
- Bosch / 11224VSR
- Bosch / 11236VS\*\*

Specifications

Cat-Class:	120-0030
AC Amps/ DC Volts:	5.7, 6.9, 7.2
Carbide Bit Capacity:	1"
Carbide Bit Capacity:	1-1/8"
Core Bit Capacity:	4"
Impact Range:	0-3900 bpm, 0-5100 bpm, 0-6150 bpm
Max. Impact Energy/Blow:	1.3ft. lbs - 2.6ft lbs
Operating Modes:	H&R / H / R
Speed Range(s):	0-1100 rpm, 0-650 rpm, 0-880 rpm
Tool Type:	SDS-plus
Weight:	6lbs - 9lbs

Quoted delivery and pick up fees are estimates. Other fees and taxes may apply. Actual delivery charges will be quoted when the order is confirmed based on the rental location.

A member of our team will contact you within 2 business hours with confirmation of your reservation.

[Home](#) | [Equipment](#) | [Locations](#) | [Customer Service](#) | [About](#) | [Site Map](#) Find us on Facebook

© 2015 Sunbelt Rentals, Inc. All Rights Reserved | [Privacy Policy](#) | [Terms and Conditions](#) | Sunbelt Rentals Toll-Free 1-800 No Sweat (800-667-9328)  
Site extended for U.S. Customers Only



More to do  
More doing

Your Store **Jacksonville #6346**  
Use My Current Location or find store


[Tool & Truck Rental](#) [Installation Services and Repair](#) [Gift Cards](#) [Help](#)

Tapcon Model # 24330 Internet # 100098197 Store SKU # 165739

### 1/4 in. x 2-3/4 in. Polymer Plated Steel Hex-Washer-Head Indoor/Outdoor Concrete Anchors (75-Pack)

\*\*\* (2) [Write a Review](#) [Ask a Question](#)


**\$23.61** / each



#### MORE IN THIS COLLECTION FROM TAPCON (27)

YOUR CURRENT PRODUCT

1 of 9




**\$23.61** / each

Tapcon 1/4 in. x 2-3/4 in. Polymer Plated...

(2)


Item Selected



**\$19.86** / each

Tapcon 1/4 in. x 2-1/4 in. Hex-Washer-Head...

Select This Item



**\$15.41** / each

Tapcon 1/4 in. x 1-1/4 in. Hex-Washer-Head...

(2)

Select This Item



**\$12.48** / each

Tapcon 1/4 in. x 2-3/4 in. Climatesal Steel...

Select This Item

1 Item(s) Selected

**ADD ITEMS TO CART**

#### PRODUCT OVERVIEW Model # 24330 Internet # 100098197 Store SKU # 165739

Tapcon is the original masonry anchor designed for fastening applications in concrete, block, and brick. Use Tapcon anchors to attach electrical equipment, two by fours, downspout straps, hose reels, flag poles, hurricane shutters, and more. The Blue Climatesal coating provides extended corrosion protection and makes Tapcon anchors perfect for outdoor use.

- Great for fastening applications in concrete, block and brick
- Use to attach electrical equipment, lumber, downspout straps, hose reels, flag poles and hurricane shutters
- Approved for treated lumber
- Made of steel with blue climatesal coating for corrosion resistance



More saving.  
More doing.

Your Store: **Jacksonville #6346**  
Use My Current Location or find store

[Tool & Truck Rental](#) [Installation Services and Repair](#) [Gift Cards](#) [Help](#)

Model # 914703 Internet # 100322321 Store SKU # 914703

# 1 in. x 4 in. x 10 ft. Common Board

★★★★ (1) [Write a Review](#) [Questions & Answers \(4\)](#)

**\$8.27** / piece



## ACCESSORIES (6)

### YOUR CURRENT PRODUCT

1 of 2



**\$8.27** /piece

1 in. x 4 in. x 10 ft. Common Board

(1)

Item Selected



**\$11.47** /each

Empire True Blue 9 in. Professional Torpedo...

(29)

Select This Item




**\$3.97** /each

HDX 3-1/4 in. 8-N-1 Screw Driver

(26)

Select This Item



**\$3.98** /each

3M Tekk Protection Clear Eye Protector...

(5)

Select This Item

1 Item(s) Selected

**ADD ITEMS TO CART**

## PRODUCT OVERVIEW Model # 914703 Internet # 100322321 Store SKU # 914703

Every piece meets the highest grading standards for strength and appearance. This lumber is for a wide range of uses from framing of houses to basic interior finishing applications. Boards can also be used for carpentry, hobbies, furniture, shelving, and general finish work. The wood has straight grain and has uniform texture. It has low shrinkage and is worked very easily by hand and machine tools. The product is easy to glue and has good nailing and screw holding properties. The paint retention properties are good and it is fairly easily treated with preservatives.  
California residents: see Proposition 65 Information

- Each piece of this lumber meets the highest quality grading standards for strength and appearance
- Boards can also be used for carpentry, hobbies, furniture, shelving, and general finish work
- This lumber can be primed and painted or stained
- Interior or exterior use

