SUBJECT: **RFQ FOR DESIGN-BUILD SVCS FOR HORIZONTAL/CIVIL ENGINEERING PROJECTS**

BID # **CDB-0006-16** OPEN DATE: **10/21/2015**

# COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
**CONSTRUCTION – DESIGN/BUILD**

AGENCY: **DEPARTMENT OF PUBLIC WORKS**

BASIS OF AWARD: **QUALIFICATIONS BASED**

NUMBER OF BIDS INVITED: - NUMBER RECEIVED: - OTHER: -

## SUMMARY OF BIDS AND RECOMMENDED ACTIONS:

The Ocean Street Drainage Improvements project was awarded to J.B. Coxwell Contracting, Inc., on 12/20/18 in the amount of $337,578.18.

Recommend approval of Change Order #1 to J. B. Coxwell Contracting, Inc., in the amount of $285,361.33, to address the increased construction costs due to design modifications required to address unknown utility conflicts and will provide 100% design, permitting and construction for the modifications. This incorporates the attached, scope and fee summary, Exhibit "Y-2", for a revised guaranteed maximum price of $622,939.51, which includes a contingency of $20,000.00 and allows for a project completion of 120 days for design and permitting and an additional 90 days from the notice to proceed for construction for an additional total of 210 days. Total annual expenditure amount is currently at $30,000,000.00; total amount spent to date is $19,427,438.05.

Funding for this award is to be executed by Amendment 23B for contract # 6533-54 and encumbered by account: 006970-565051-4-32111-384020

Attachments: Recommendation Memo, Exhibit "Y-2", Previous Award(s)

BUYER Marilyn Laidler
MARILYN LAIDLER

RESPECTFULLY SUBMITTED _____
for GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: **Robin G. Smith, P.E., Chief, Engineering and Construction Management**

---

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING_____ MEMBERS DISAPPROVING_____ DATE:_____

_____ _____ OTHER_____

_____ _____

_____ _____

_____ _____

_____ _____

---

ACTION OF AWARDING AUTHORITY DATE _____

APPROVED_____ DISAPPROVED: _____

OTHER: _____

SIGNATURE OF AUTHENTICATION _____

# City of Jacksonville, Florida

*Lenny Curry, Mayor*

Department of Public Works
Engineering & Construction Management Division
214 N. Hogan Street, 10th Floor
Jacksonville, FL 32202
(904) 255-8762
www.coj.net

ONE CITY, ONE JACKSONVILLE

November 3, 2020

TO: Gregory W. Pease
Chief of Procurement

THRU: John P. Pappas, P.E.
Director

FROM: Robin G. Smith, P.E.
Chief, Engineering and Construction Management

**SUBJECT:** CDB-0006-16 – Design-Build Services - Horizontal & Civil Engineering – Ocean Street Drainage Improvements AMENDMENT 23B

In accordance with Design/Build CDB-0006-16, Contract 6533-54, the Ocean Street Drainage Improvements project was awarded by Amendment 23A, in the amount of $337,578.18, to provide 100% design, permitting and construction related services. Amendment 23B is to address the increased construction costs due to design modifications required to address unknown utility conflicts and will provide 100% design, permitting and construction for the modifications. Negotiations have resulted in the attached Scope and Fee, Exhibit Y-2 add an additional $285,361.33 for a revised GMP amount of $622,939.51, which includes a contingency of $20,000.00 and allows for a project completion of 120 days for design and permitting and an additional 90 days from the notice to proceed for construction for an additional total of 210 days. J.B. Coxwell Contracting is committed to meeting the 10% JSEB participation goals established for this contract.

Accordingly, this is to recommend that Amendment 23 to Contract No. 6533-54, originally executed March 26, 2019, between the City and J. B. Coxwell Contracting, Inc. for Ocean Street Drainage Improvements, be amended to incorporate the attached Scope and Fee Summary, Exhibit Y-2, to increase the GMP by $285,361.33 to a new GMP amount of $622,939.51, known as Amendment 23B.

Funding for this project should be encumbered as follows:

| ACCOUNTS: | TOTAL |
|---|---|
| 006970 | |
| PWCP Public Works Capital Projects- Other Transportation Services | |
| 565051 | |
| 4 | |
| 32111-384020 | |
| $285,361.33 | $285,361.33 |

RGS/lw

Attachment: Exhibit Y-2

Cc: Lori West, Engineering and Construction Management
Kelsey Cox, P.E., Engineering and Construction Management

ab

EXHIBIT Y-2

**J.B. Coxwell Contracting, Inc.**
6741 Lloyd Road West
Jacksonville, Florida 32254
Office (904) 786-1120 Fax (904) 783-2970

June 19, 2020

Kelsey Cox, P.E.
City of Jacksonville Department of Public Works
Engineering & Construction Management Division
214 N. Hogan Street, 10th Floor
Jacksonville, Florida 32202

**Re: Scope of Services and Fee Proposal for Ocean Street Drainage Improvements (revised design) 100% Design, Permitting and Construction Services – Price Revision 4**

**Design-Build Construction Delivery for City of Jacksonville-RFQ CDB-0006-16**
**City Contract No. 6533-54**

Dear Ms. Cox:

J.B. Coxwell Contracting, Inc. (JBCCI) is pleased to submit for your review and consideration the following design-build scope of services and attached lump sum fee proposal for the revised 100% design, permitting, and construction of the above referenced project. The scope of work for 100% design, permitting, and construction services have been described in detail on the attached proposals and fee summary.

This project was previously awarded to JBCCI for the lump sum amount of Three Hundred Thirty-Seven Thousand Five Hundred Seventy-Eight Dollars and Eighteen Cents ($337,578.18) under contract 6533-54, amendment 23A. Since the design has been modified on this project to increase the scope of the services provided, JBCCI submits to you the revised lump sum amount for 100% design, permitting and construction fees of Five Hundred Forty-Six Thousand Three Hundred Seventy Dollars and Thirteen Cents ($546,370.13) which includes a project contingency of $20,000.00. The project contingency is for project elements which have not been fully designed and permitted, and which may increase in quantity or cost during the final design phase or during construction. The project contingency is for the Design-Builder's benefit and not for changed field conditions, unknown field conditions or added scope of work.

The project funding included in contract amendment 23A has not been billed 100%, rather we have only invoiced for approximately $76,569.38 for the original design/permit fees and a percentage of design build fees. This amount would need to be added to the proposed total estimate of $546,370.13 for a projected total expenditure of $622,939.51 for this project. The COJ will need to issue another contract amendment for this project in the amount of Two Hundred Eighty-Five Thousand Three Hundred Sixty-One Dollars and Thirty Three Cents ($285,361.33) to fund the re-design and construction of the revised drainage scope included for this project.

The design and permitting for the revised scope will require one hundred twenty (120) days to complete and construction can be completed within ninety (90) calendar days after we receive the construction notice to proceed.

EXHIBIT A-2

This lump sum proposal is inclusive of only those services noted on the attached proposals and which are anticipated at this time. No services or work other than those noted in the proposals are included. In addition, any unknown condition(s) which may surface during design and construction or any other increase in scope of services may result in a request for additional services. No work will proceed however, without first obtaining approval from the City for any additional services.

We are again very appreciative of the opportunity to provide you with our design-build services. Should you have any questions or need any further information, please do not hesitate to contact us. We are also available to review and discuss this proposal with you and/or others at your convenience.

Regards,

*J.B. Coxwell Contracting, Inc.*

Jayson Smith

Jayson Smith,
Design Build Manager

*Building Efficiency Together*

# FEE SUMMARY

J.B. Coxwell Contracting, Inc.
6741 Lloyd Road West
Jacksonville, Florida 32254
Ph. (904) 786-1120
Contact: Jayson Smith, Design Build Manager
JaysonS@JBCoxwell.com

6-19-2020

Revision 3

QUOTE City of Jacksonville
TO Department of Public Works

| JOB | LOCATION | START DATE |
|---|---|---|
| Ocean Street Drainage Improvements (Bay to Forsyth) | Jacksonville, Florida | October 2020 |

| ITEM | DESCRIPTION | QTY | UNIT | UNIT PRICE | EXT PRICE |
|---|---|---|---|---|---|
| 1 | General Conditions | 1 | LS | $ 47,690.00 | $ 47,690.00 |
| 10 | Maintenance of Traffic | 1 | LS | $ 32,621.00 | $ 32,621.00 |
| 20 | Erosion Control | 1 | LS | $ 3,500.00 | $ 3,500.00 |
| 30 | Site Preparation & Demolition | 1 | LS | $ 25,651.00 | $ 25,651.00 |
| 40 | Dewatering for Drainage Construction | 1 | LS | $ 52,470.00 | $ 52,470.00 |
| 45 | Drainage Bypass Pumping During Construction | 13 | DA | $ 444.34 | $ 5,776.42 |
| 50 | Tie-Into Existing Drainage Structure | 1 | EA | $ 13,588.55 | $ 13,588.55 |
| 60 | Install Drainage Pipe | 306 | LF | $ 203.63 | $ 62,310.78 |
| 65 | Install Drainage Structures | 5 | EA | $ 15,971.00 | $ 79,855.00 |
| 90 | Install Flowable Fill w/ Temporary Road Plates at Structures | 160 | CY | $ 271.38 | $ 43,420.80 |
| 95 | Remove & Replace Unsuitable Fill in Trench | 300 | CY | $ 30.00 | $ 9,000.00 |
| 100 | Restore Roadway Subgrade & Base in Patch Area | 670 | SY | $ 65.01 | $ 43,556.70 |
| 120 | Replace Curb & Gutter | 200 | LF | $ 26.19 | $ 5,238.00 |
| 125 | Replace Sidewalk (Plain) | 50 | SY | $ 72.86 | $ 3,643.00 |
| 130 | Replace Asphalt Pavement (2" Thickness) | 670 | SY | $ 31.50 | $ 21,105.00 |
| 140 | Replace Striping (Painted Markings) | 1 | LS | $ 2,625.00 | $ 2,625.00 |
| 200 | Misc. Final Clean-Up | 1 | LS | $ 3,144.57 | $ 3,144.57 |
| 300 | GAI Re-Design Fees | 1 | LS | $ 20,879.00 | $ 20,879.00 |
| 400 | Construction Contingency | 1 | LS | $ 20,000.00 | $ 20,000.00 |
| 450 | 100% Payment & Performance Bond | 1 | LS | $ 4,960.75 | $ 4,960.75 |
| 500 | Design Build Fee | 1 | LS | $ 45,334.56 | $ 45,334.56 |
| | Revised design and construction pricing subtotal | | | TOTAL: | $546,370.13 |

| | |
|---|---|
| Previously Spent Fees for this Project with JBCCI | $ 76,569.38 |
| Total Estimate for this Project | $622,939.51 |
| Previously Issued Contract Amendment 23A | ($337,578.18) |
| Additional Fees Required to Complete this project as Revised | $285,361.33 |

Clarifications/ Exclusions;

- Estimate is based on GAI's updated design and engineering fees as shown in the proposal dated 1-23-20, added fees (verbal), GAI's revised drainage sketch attached. All notes, exclusions, and clarifications contained in the GAI proposal apply to the JBCCI proposal.
- Existing private and public utility locates, identification, protection, isolation, and relocation by others (including but not limited to electric, water, sewer, cable, telephone, misc. communications, traffic signal, street lighting, gas, fiber optic cables, etc.)
- Contingency fee included for construction and design aspects not known at the time of the proposal preparation
- This estimate excludes unknown subsurface debris removal/ disposal
- This estimate includes up to 300 CY of unsuitable soil removal/ replacement, if we encounter additional unsuitable soil the balance will be billed against the construction contingency
- This estimate excludes any work associated with the discovery or handling of hazardous or non-hazardous waste that may be encountered while constructing the drainage improvements on this project
- All public notices and informational meetings to be handled by the COJ
- JBCCI provides this pricing with the assumption that all work will be authorized and performed with one mobilization
- This proposal pricing is valid for 30 days from date of revision
- Asphalt, curb, and sidewalk removal/replacement is included for the specific areas impacted for the new construction Only. There are no allowances included for asphalt milling/ resurfacing or other hardscape repairs within the project area.

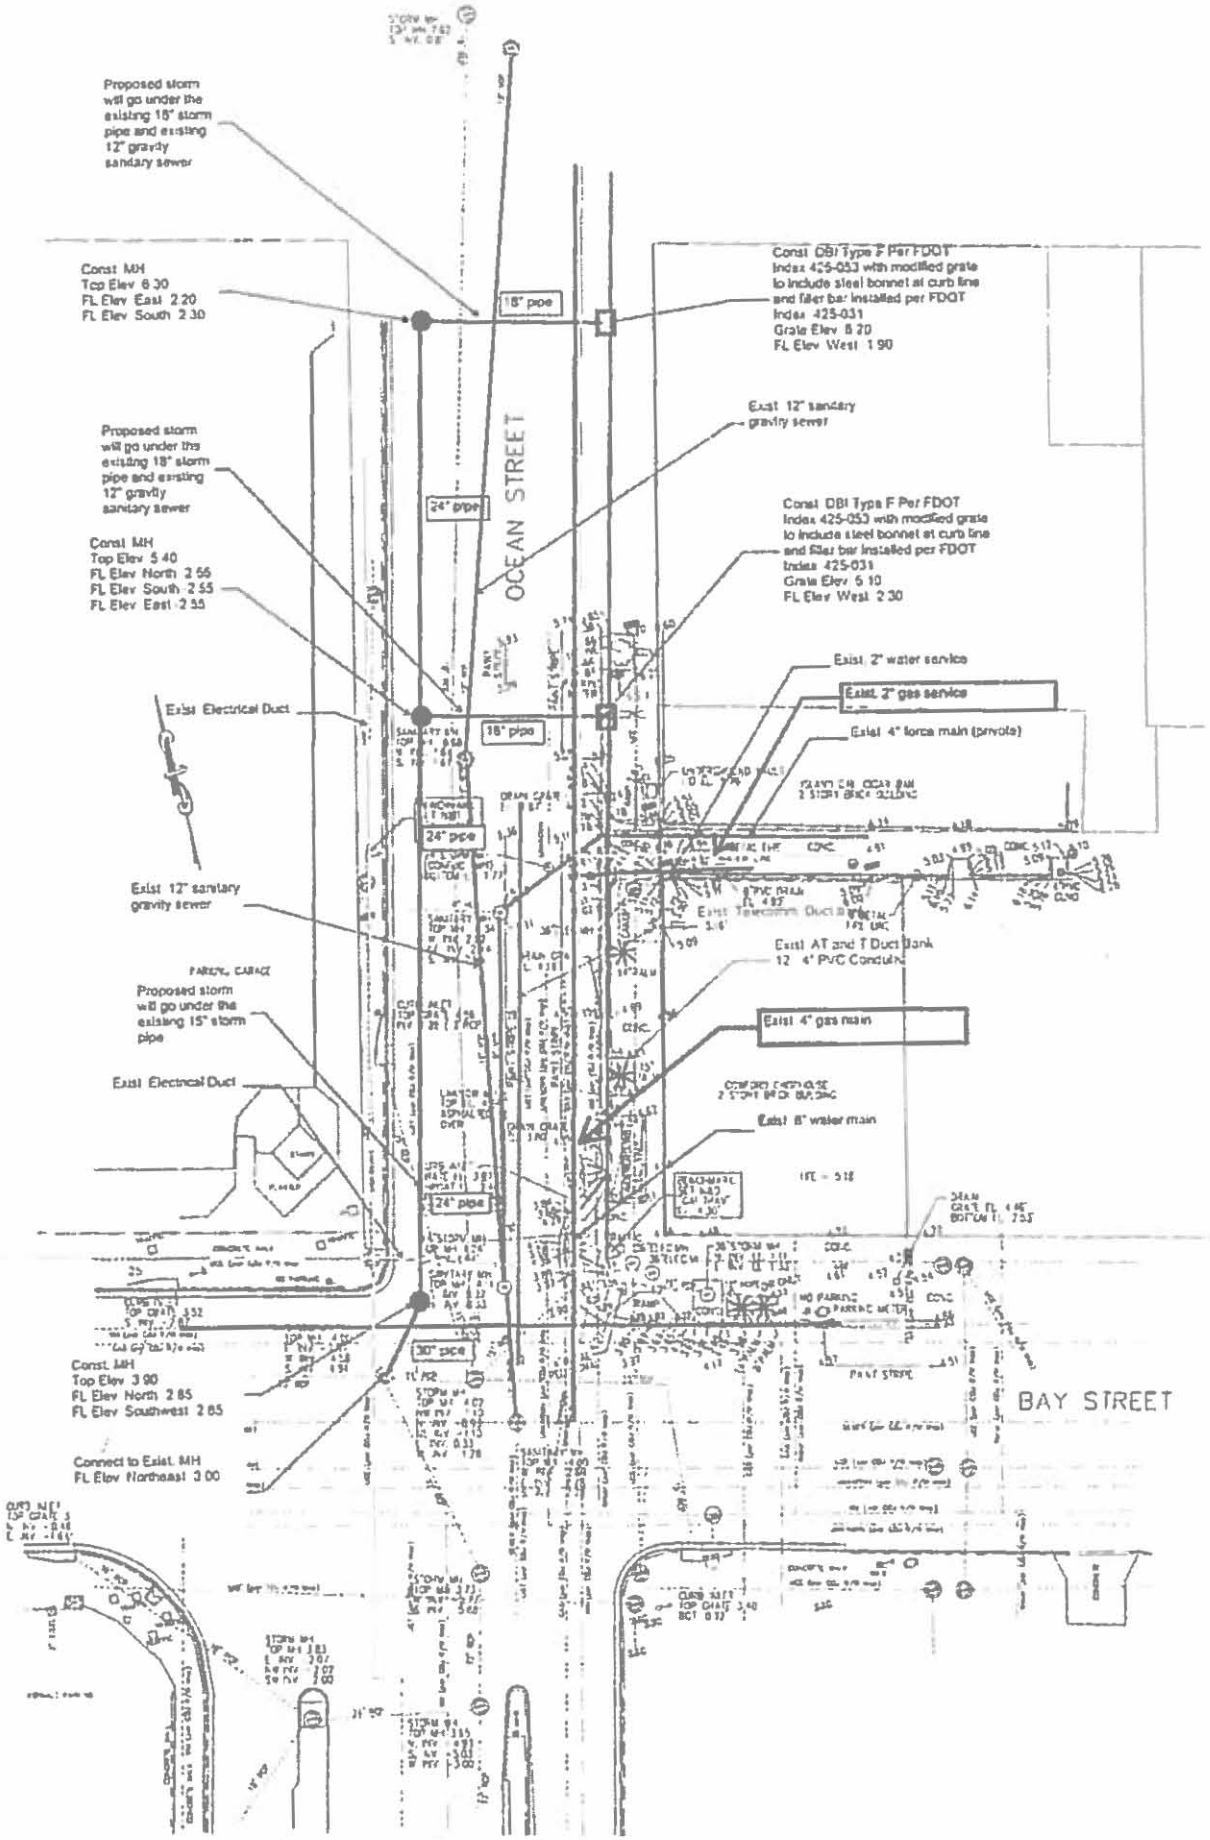
Proposed storm will go under the existing 18" storm pipe and existing 12" gravity sanitary sewer
Const MH
Top Elev 6 30
FL Elev East 2 20
FL Elev South 2 30
18" pipe
Const DBI Type F Per FDOT Index 425-053 with modified grate to include steel bonnet at curb line and filler bar installed per FDOT Index 425-031
Grate Elev 6 20
FL Elev West 1 90
Exist 12" sanitary gravity sewer
OCEAN STREET
Proposed storm will go under the existing 18" storm pipe and existing 12" gravity sanitary sewer
24" pipe
Const MH
Top Elev 5 40
FL Elev North 2 55
FL Elev South 2 55
FL Elev East 2 55
Const DBI Type F Per FDOT Index 425-053 with modified grate to include steel bonnet at curb line and filler bar installed per FDOT Index 425-031
Grate Elev 5 10
FL Elev West 2 30
Exist 2" water service
Exist 2" gas service
Exist Electrical Duct
18" pipe
Exist 4" force main (private)
24" pipe
Exist 12" sanitary gravity sewer
Exist AT and T Duct Bank
12 4" PVC Conduits
Proposed storm will go under the existing 15" storm pipe
Exist 4" gas main
Exist Electrical Duct
Exist 8" water main
24" pipe
30" pipe
Const MH
Top Elev 3 90
FL Elev North 2 85
FL Elev Southwest 2 85
Connect to Exist MH
FL Elev Northeast 3 00
BAY STREET

**EBO FORM 1**
**SCHEDULE OF SUBCONTRACTOR/SUBCONSULTANT PARTICIPATION**

Name of Proposer: J.B. Coxwell Contracting, Inc.

Project Title: Design-Build Services for Ocean Street Drainage Improvements (Revised Scope)

Proposal Number: 6533-54 - Amendment 23B

Total Base Proposal Amount (if applicable): $285,361.33

***Please list all JSEBs first**

| Full Company Name | JSEB Category (African-American, Women, Asian, Native American, Non-MBE or Hispanic) | Type of Work to be Performed | Total Contract Value or Percentage |
|---|---|---|---|
| | | | |
| | | | |
| Meskell & Asociates | Woman | Geotechnical, Engineering | 1% |
| Donna Hamilton, Inc. | Woman | Precast Drainage Structures & Pipe | 8% |
| D.J. Contracting, Inc. | Woman | Trucking/ Hauling | 4% |
| | | | |
| | | | |
| | | | |
| | | | |

Attach additional list of subcontractors/sub-consultants as needed

| CONSULTANT/SUBCONTRACTOR/SUPPLIER TOTAL VALUES | |
|---|---|
| African-American Participation Total | |
| Hispanic-American Participation Total | |
| Native-American Participation Total | |
| Asian-American Participation Total | |
| Woman Participation Total | 13% |
| Non-MBE Participation Total | 87% |

The undersigned will enter into a formal Agreement with the JSEB Suppliers/Consultants/Subcontractors identified herein for work listed in this schedule conditioned upon execution of a contract with the City of Jacksonville. Under penalties of perjury I declare that I have read the foregoing conditions and instructions and the facts are true to the best of my knowledge and beliefs.

Signature of Proposer: Jayson Smith

Title: Design Build Manager

Date: September 16, 2020

Print Name: Jayson Smith

SUBJECT: **RFQ FOR DESIGN-BUILD SVCS FOR HORIZONTAL/CIVIL ENGINEERING PROJECTS**

BID # **CDB-0006-16** OPEN DATE: **10/21/2015**

## COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
**CONSTRUCTION – DESIGN/BUILD**

AGENCY: **DEPARTMENT OF PUBLIC WORKS**

BASIS OF AWARD: **QUALIFICATIONS BASED**

NUMBER OF BIDS INVITED: - NUMBER RECEIVED: - OTHER: -

**SUMMARY OF BIDS AND RECOMMENDED ACTIONS:**
The Department of Public Works has completed negotiations with J.B. Coxwell Contracting, Inc., for the Ocean Street Drainage Improvements project in accordance with subject bid.

Recommend approval of award to J. B. Coxwell Contracting, Inc., in the guaranteed maximum price not-to-exceed $337,578.18, which includes a contingency of $30,000.00. The scope of award is to provide 100% design, permitting and construction related services for Ocean Street Drainage Improvements. This incorporates the attached, scope and fee summary, Exhibit "Y-1", with guaranteed completion of 200 days from issuance of notice-to-proceed.

Funding for this award is to be executed by Amendment 23A for contract # 6533-54 and encumbered by account: PWCP331SD541-06505-PW0718-01-PWC023-18- $148,000.00; DICP363-06505-PW0718-01- $40,796.93; DICP322-06505-PW0718-01- $145,116.97; PWEN462SW-06505-PW0072-01- $3,664.28

Attachments: Recommendation Memo, Exhibit "Y-1", Previous Award(s)

BUYER MARILYN LAIDLER

RESPECTFULLY SUBMITTED GREGORY PEASE, CHIEF PROCUREMENT DIVISION

CONCURRENCE BY: **Ed Starnes, P.E., J.D., Acting Chief, Engineering and Construction Management**

---

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING Ø DATE: 12/20/18

OTHER

---

ACTION OF AWARDING AUTHORITY DATE 12/20/18

APPROVED DISAPPROVED:

OTHER:

SIGNATURE OF AUTHENTICATION

Sam E. Mousa
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:
Executive Order No. 2015-05

SUBJECT: **RFQ- FOR DESIGN- BUILD SERVICES OF HORIZONTAL/CIVIL ENGINEERING PROJECTS**

BID # **CDB-0006-16** OPEN DATE: **10/21/2015**

## COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
**CONSTRUCTION – DESIGN/BUILD**

AGENCY: **DEPARTMENT OF PUBLIC WORKS**

BASIS OF AWARD: **EVALUATION CRITERIA**

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 5 OTHER: 1

**SUMMARY OF BIDS AND RECOMMENDED ACTIONS:**
The City had previously issued this RFP, and the evaluation committee has evaluated proposals. Subsequently, presentations were conducted and evaluated on January 28, 2016; 02/04/16 J.B. Coxwell Contracting, Inc., was awarded as highest ranking firm with funding not-to-exceed $6,000,000.00 annually for a period of service for five (5) years.

Recommend approval of award to include the rate sheets as part of Exhibit A, as they were omitted from original award. No additional changes needed.

To be executed by formal contract through Office of General Counsel.

Attachments: Recommendation Memo, Previous Award(s)

BUYER MARILYN LAIDLER

RESPECTFULLY SUBMITTED GREGORY FEASE, CHIEF PROCUREMENT DIVISION

CONCURRENCE BY: **Thomas N. Fallin, P.E., Chief, Engineering & Construction Management Division**

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING _____ DATE: 6-16-16

OTHER _____

ACTION OF AWARDING AUTHORITY DATE 6/16/16

APPROVED ✓ DISAPPROVED: _____

OTHER: _____

SIGNATURE OF AUTHENTICATION

Sam E. Mousa
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of
Executive Order No. 2015-05

SUBJECT: **RFQ- FOR DESIGN- BUILD SERVICES OF HORIZONTAL/CIVIL ENGINEERING PROJECTS**

BID # **CDB-0006-16** OPEN DATE: **10/21/2015**

# COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
**CONSTRUCTION – DESIGN/BUILD**

AGENCY: **DEPARTMENT OF PUBLIC WORKS**

BASIS OF AWARD: **EVALUATION CRITERIA**

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 5 OTHER: 1

## SUMMARY OF BIDS AND RECOMMENDED ACTIONS:

The City had previously issued this RFP, and the evaluation committee has evaluated proposals. Subsequently, presentations were conducted and evaluated on January 28, 2016. Based upon the combination of proposal and presentation evaluations, scores and rankings are as follows (Listed in alphabetical order):

2) Archer-Western – 118.25
3) Callaway Contracting, Inc. - 100
1) J.B. Coxwell Contracting, Inc. - 121.5

Recommend approval of award to J.B. Coxwell Contracting, Inc., as receiving the highest score in accordance with the evaluation and ranking above. Period of Service will be five (5) years from effective date of contract with funding not-to-exceed $6,000,000.00 annually. To be executed by formal contract through Office of General Counsel.

Attachments: Recommendation Memo, Scoring Matrix, Previous Award

BUYER Marilyn Laidler
MARILYN LAIDLER

RESPECTFULLY SUBMITTED
GREGORY REASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: **Thomas N. Fallin, P.E., Acting Chief-Engineering & Construction Management Division**

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING _____ DATE: 2/4/16

OTHER _____

ACTION OF AWARDING AUTHORITY DATE 2/04/16

MR APPROVED ✓ DISAPPROVED: _____

Sam E. Mousa
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:
Executive Order No. 2015-05

OTHER: _____

SIGNATURE OF AUTHENTICATION _____

SUBJECT: **RFQ- FOR DESIGN- BUILD SERVICES OF HORIZONTAL/CIVIL ENGINEERING PROJECTS**

BID # **CDB-0006-16** OPEN DATE: **10/21/2015**

# COMPETITIVE SEALED PROPOSAL EVALUATION COMMITTEE

KIND AND BASIS OF CONTRACT:
**CONSTRUCTION – DESIGN/BUILD**

AGENCY: **DEPARTMENT OF PUBLIC WORKS**

BASIS OF AWARD: **EVALUATION CRITERIA**

NUMBER OF BIDS INVITED: 5 NUMBER RECEIVED: 5 OTHER: 1

## SUMMARY OF BIDS AND RECOMMENDED ACTIONS:

The City had previously issued this RFP, and the evaluation committee has evaluated proposals. Based upon the proposal evaluation, the average scores and rankings are as follows (Listed in alphabetical order):

2) Archer-Western Contractors, LLC. – 91
1) J.B. Coxwell Contracting- 92
3) Callaway Contracting- 74

Pursuant to Section 2.6 – Award of Contract of the RFP, recommend approval to conduct formal interviews with each of the three-top ranked Firms.

Attachments: Recommendation Memo, Scoring Matrix, Bid Tabulation, Section 2.6, JSEB Letter

BUYER Marilyn Laidler
MARILYN LAIDLER

RESPECTFULLY SUBMITTED
GREGORY PEASE, CHIEF
PROCUREMENT DIVISION

CONCURRENCE BY: **William J. Joyce, P.E., Chief-Engineering & Construction Management**

---

**(ALL AWARD ACTIONS SUBJECT TO LAWFULLY APPROPRIATED FUNDS)**
ACTION OF CSPEC COMMITTEE ON RECOMMENDATIONS ABOVE

MEMBERS APPROVING 5 MEMBERS DISAPPROVING _____ DATE: 12-30-15

OTHER _____

---

ACTION OF AWARDING AUTHORITY DATE 1/01/16

APPROVED ✓ DISAPPROVED: _____

OTHER: _____

SIGNATURE OF AUTHENTICATION

Sam E. Mousa
Chief Administrative Officer
For: Mayor Lenny Curry
Under Authority of:
Executive Order No. 2015-05
